

Community Update – July 19, 2023


Milneburg Group A

The Milneburg Group A project (RR130) was launched in June of 2020 and occurred alongside the Milneburg Group B Full Reconstruction project (RR131), which is now complete. Milneburg Group A includes over 245 blocks that are receiving construction on the subsurface utilities and/or roadway. The majority of work conducted under this project is considered Incidental Road Repairs and Patch Mill/Overlay where roadway restoration primarily occurs alongside utility repairs or installation of ADA ramps.

Early in the construction process and continuing through now, crews from Command Construction Industries, LLC, have discovered utility and roadway failures that have required an increase to the scope of the project via plan changes coordinated with DPW and SWBNO partners. These plan changes have included waterline and utilities work that has extended into major thoroughfares, as well as increases to the depth and scope of roadway repairs to ensure that the planned work adequately addresses these unexpected conditions. The most common plan changes submitted for this project have upgraded the roadway restoration from Patch Mill and Incidental Road Repairs to Full Depth restoration that rebuilds the roadway rather than surface level repairs.

30-Day Forecast

The majority of utility and drainage work has been completed and all identified water leaks are being addressed in coordination with SWBNO. Water leaks were identified at the following locations: Prentiss and Baccich; Arts and Vienna; Prentiss and Eads; Prentiss and Franklin; Arts and Pressburg; 5900 Arts; 2500 Vienna; 2750 Prentiss; 6000 Arts; Athis and Marigny; 6200 Mandeville; Pressburg and Spain; and 5912 Spain. Crews will be focusing on completing the remaining paving and sidewalk and driveway work throughout the site in Zones 1, 5, 6, 7, 8 and 9 (see Zone Map below for reference and project limits).

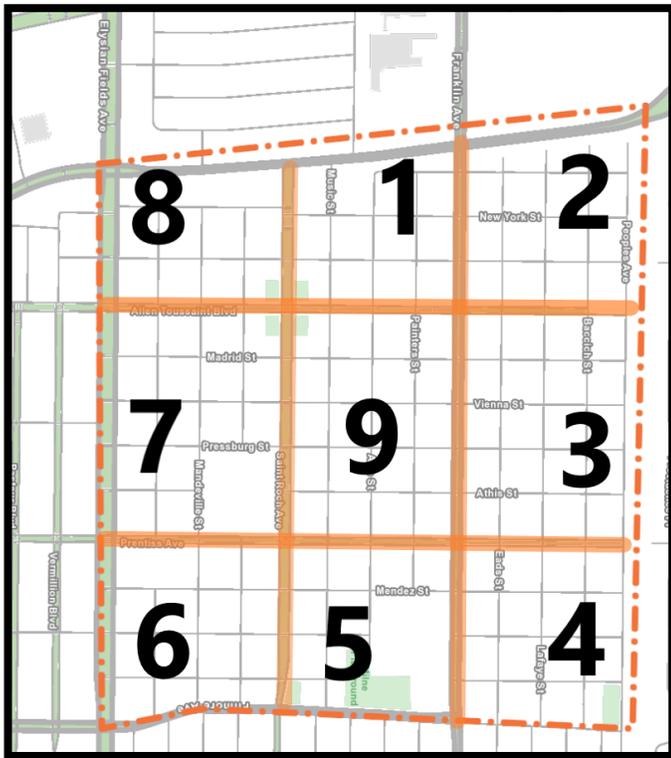

This includes completion of remaining paving on Elysian Fields, Franklin Ave and Music St. Sidewalk and driveway work will continue and complete in Zone 8 (west of St. Roch Ave and North of Allen Toussaint Blvd). The project areas south of Leon C. Simon Dr and east of Franklin Ave are largely complete and are being cleaned up and closed out.

This **\$15.4M** Milneburg Group A project began in June 2020 and is expected to complete in Fall of 2023. The project was designed by Mott Macdonald, and is being constructed by Command Construction Industries, LLC. The scope of work varies block by block but includes the following:

- Replacement of damaged underground water, sewer and drainage lines;
- Repaving the roadways;
- Replacing damaged sidewalks and driveway aprons; and
- Installing Americans with Disabilities Act-compliant curb ramps at intersections.

How to Stay Informed

Questions about this project may be directed to roadwork@nola.gov or to our RoadworkNOLA hotline 504.658.ROAD (7623) or **sign up for RoadworkNOLA text alerts by texting ROADWORK to 77295, or go to ready.nola.gov/alerts to create a whole profile and select the “roadwork” alert list.**
